


### CHAPTER 3: Project Management – Exercises from book

- **3.7** Draw the AON project network using the following information:

ACTIVITY	IMMEDIATE PREDECESSOR(S)	DURATION (WEEKS)
A	—	4
B	—	35
C	—	5
D	A	9
E	B	3
F	C, E	1
G	D	2
H	F	3
I	G, H	15
J	G	1

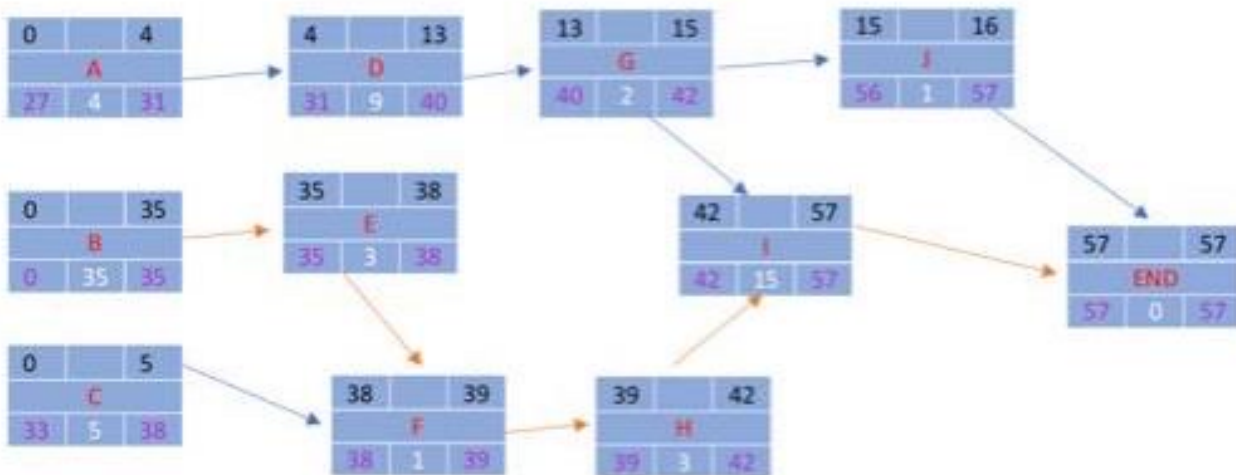

It takes **57 weeks** to complete the project

Critical path: B - E - F - H - I
